Project Scope

- Construct ramp pavement to the west of future footprint of Terminal F up to and adjoining Taxiway G
- Construction began in January 2017
- Taxiway G closure (Phase 2) COMPLETED
- Jet fuel vault and deicing pad (Phase 1) COMPLETED

Project Status

- Phase 3 remaining
- Project completion in Fall 2018






During construction:


Taxiway G will be closed during Phase 2.


A380 deice operations must take place at the southwest hold pad during Phase 1.

Minimal operational impacts involving Phase 3.

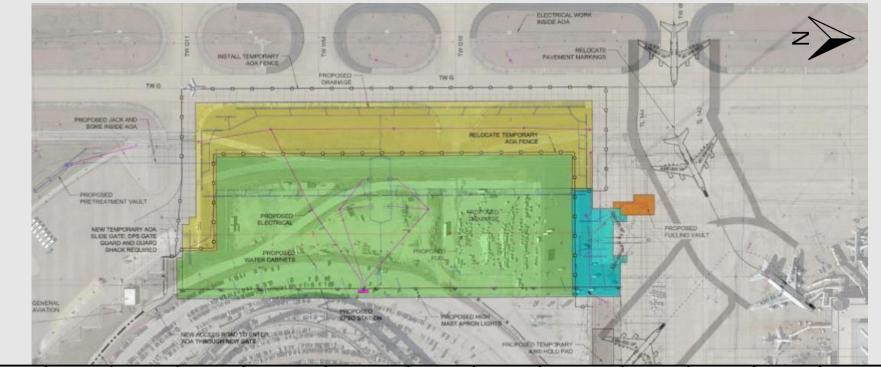

											2018				
	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May
	/6 /13 /20	/3 /10 /24	/1 /8 /22 /23	/5 /12 /13 /26	/3 /10 /17 /24	/31 /7 /14 /21	/28 /4 /11 /18 /25	0/2 0/16 0/23 0/20	/6 /13 /20 /27	2/4 2/11 2/15 2/25	1 15 22 22	15 112 113 126	/5 /12 /13	/2 /16 /23	4/30 5/7 5/14 5/21
	0 0 0 0	4 4 4 4	ធីធីធីធីធី	0000	6 6 6 6		<u>യ ന ന ന ന</u>	2 2 2 2 2 2	= = = = =	5 2 5 5 5	2 2 2 2 2 2	ରା ଭିର୍ବ ଭି	0 0 0 0	* * * *	4 6 6 6
Phase 1/1A (completed)															
Phase 2 (completed)	Taxiway G Closure														
Phase 3															

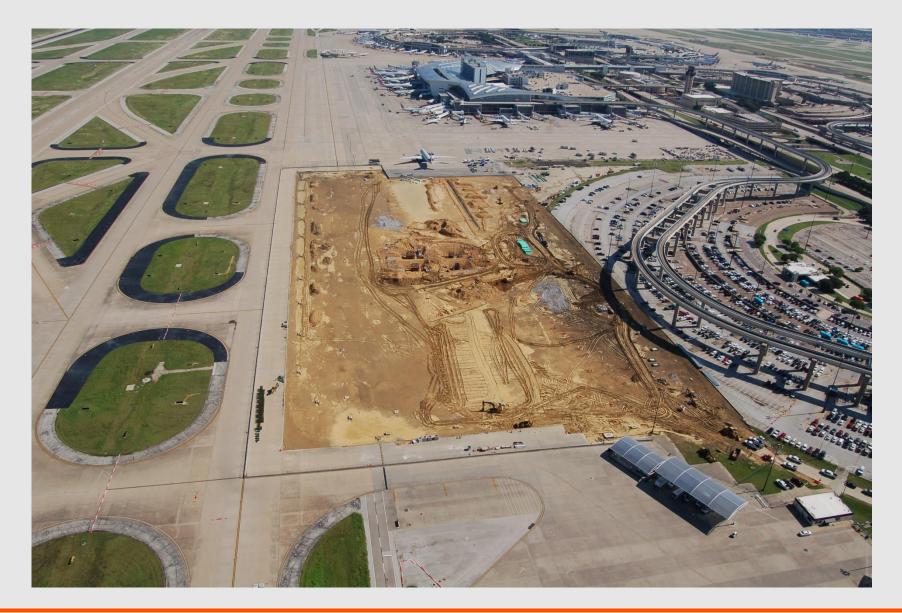

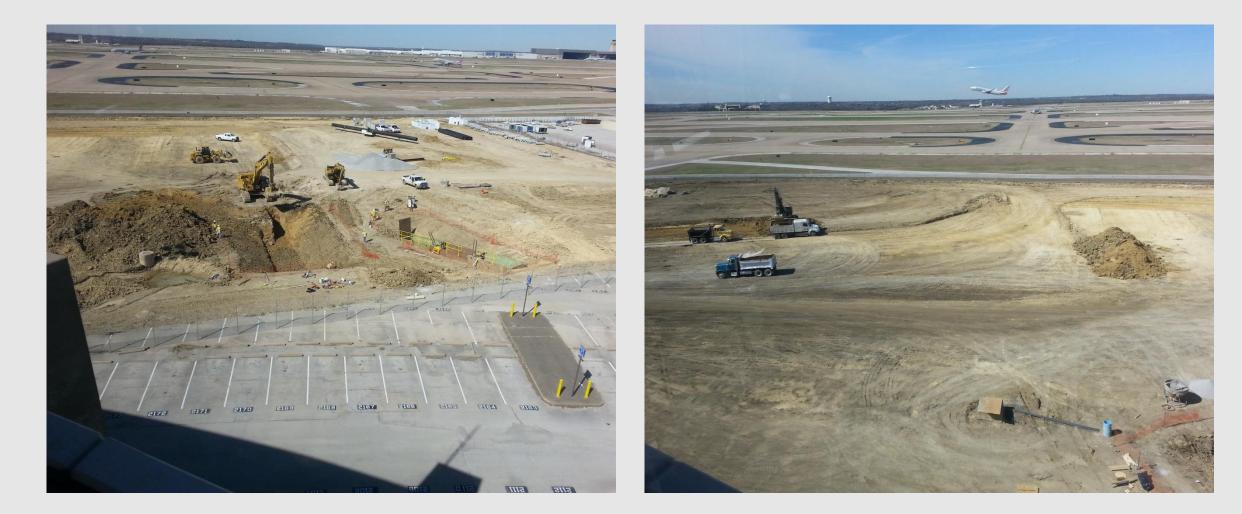



Construction of new jet fuel vault

