



Construction Safety Inspection Checklist

Complete

Score	66 / 68 (97.06%)	Flagged items	0	Actions	2
Document No.	3542352				
Conducted on	19 Oct 2023 20:24 PST				
Prepared by	Sokha Jason				
Location	Los Angeles, CA, USA (34.0549076, -118.242643)				
Personnel	Nadir Fidelis Erzsi Şerife Mariasole Fresh Freak Enid Friedhold				

Actions

2 actions

Audit / PROGRAM ADMINISTRATION

1.2 Are emergency numbers and contacts posted?

No

They are missing.

To do | Priority: Medium | Due: 26 Oct 2023 20:25 PST | Created by: SafetyCulture Staff

Put up a new poster for emergency numbers and contacts

Audit / HOUSEKEEPING

2.1 Work areas orderly and clean

No



Photo 1

To do | Priority: High | Due: 26 Oct 2023 20:26 PST | Created by: SafetyCulture Staff

Get more cleaners

Audit		2 actions, 66 / 68 (97.06%)
PROGRAM ADMINISTRATION		1 action, 4 / 5 (80%)
1.1 Are OSHA guidelines in clear view and have been communicated well?	Yes	
1.2 Are emergency numbers and contacts posted?	No	
They are missing.		
To do Priority: Medium Due: 26 Oct 2023 20:25 PST Created by: SafetyCulture Staff		
Put up a new poster for emergency numbers and contacts		
1.3 Have toolbox talks been conducted?	Yes	
1.4 Are emergency action plans posted and up to date?	Yes	
1.5 Are all emergency life-saving equipment in place?	Yes	
HOUSEKEEPING		1 action, 3 / 4 (75%)
2.1 Work areas orderly and clean	No	
		
Photo 1		
To do Priority: High Due: 26 Oct 2023 20:26 PST Created by: SafetyCulture Staff		
Get more cleaners		
2.2 Adequate lighting	Yes	
2.3 Job site free of slips, trips and fall hazards	Yes	
2.4 Break areas orderly	Yes	
ELECTRICAL / UTILITY		7 / 7 (100%)
3.1 Insulation intact on cords and wiring	Yes	
3.2 Temporary lighting guarded	Yes	
3.3 Electrical panels labeled and covered accordingly	Yes	
3.4 Ground-Fault Circuit Interrupter (GFCI) protection utilized	Yes	

3.5 Underground electrical lines marked	Yes
3.6 Underground gas lines marked	Yes
3.7 Lockout procedures utilized	Yes
HAND AND POWER EQUIPMENT	4 / 4 (100%)
4.1 Hand tools in good working order	Yes
4.2 Electrical cords in good working order	Yes
4.3 All mechanical safeguards in use	Yes
4.4 Handles not broken and are splinter free	Yes
EQUIPMENT	6 / 6 (100%)
5.1 Breaks, lights, signals and alarms operative	Yes
5.2 Daily log book filled out	Yes
5.3 Seat belts worn	Yes
5.4 Aerial lift - PPE being used	Yes
5.5 Cranes- swing radius protected - level	Yes
5.6 Rigging equipment inspected - tag showing	Yes
BARRICADES AND FENCING	4 / 4 (100%)
6.1 Roadways and sidewalks protected	Yes
6.2 Floor openings planked or barricaded	Yes
6.3 Wall, roof openings covered or barricaded	Yes
6.4 Leading edges guarded	Yes
EXCAVATION	3 / 3 (100%)
7.1 Necessary ladders provided	Yes
7.2 Spoil set back at least 2 feet	Yes
7.3 Rebar impalement protection	Yes

LADDERS		5 / 5 (100%)
8.1 Ladders in good condition		Yes
8.2 Side rails extend well above landing		Yes
8.3 Proper for job and secure		Yes
8.4 Step ladders fully open when in use		Yes
8.5 Placement of ladder safe		Yes
INFECTION CONTROL		4 / 4 (100%)
9.1 Daily inspection checklist completed		Yes
9.2 Interim Life Safety Measures (ILSM) updated		Yes
9.3 Debris covered		Yes
9.4 Walk off mats in place and in use		Yes
SCAFFOLDING		11 / 11 (100%)
10.1 All scaffolds plumbed and leveled as erection proceeds		Yes
10.2 Are adequate sills and base plates being used		Yes
10.3 If electrical power lines are near the scaffold, are necessary precautions being taken		Yes
10.4 Do scaffold planks extend past their end supports not less than 6 inches and no more than 12 inches		Yes
10.5 Are guardrails and end rails in place		Yes
10.6 To protect from falling objects, are toe boards or area barricaded below		Yes
10.7 Are frames and panels braced by cross, horizontal or diagonal braces		Yes
10.9 Is fall protection being used in areas where required		Yes
10.10 Are scaffolds securely anchored at lease every 30 feet of length and 25 feet in height		Yes
10.11 Is their an assess ladder, steps or equivalent safe access to scaffold		Yes

10.12 Is the scaffold within its weight capacity	Yes
ENVIRONMENTAL CONTROLS	3 / 3 (100%)
11.1 Silt fence installed and maintained	Yes
11.2 Hazardous materials properly stored	Yes
11.3 Spill containment kit adequate / on site	Yes
FIRE PREVENTION	4 / 4 (100%)
12.1 Are safety cans being used and properly labeled	Yes
12.2 Propane tanks - barricade installed - labeled - (flammable,no smoking, fuel type)	Yes
12.3 Compressed gas cylinders secured- upright- protected from damage	Yes
12.4 Fire extinguishers immediately available and inspection current	Yes
PPE	8 / 8 (100%)
13.1 Hard hats worn	Yes
13.2 Gloves available - cut resistant for demo	Yes
13.3 Face shields being used - mason saw or other operations	Yes
13.4 Eye protection	Yes
13.5 Hearing protection	Yes
13.6 Safety harness and lanyards utilized with adequate anchorage points	Yes
13.7 Respirators and masks utilized	Yes
13.8 High visible clothing in use	Yes
Any violations?	Yes
What are the violations?	
- Dirty workplace - Lack of emergency contacts	
Sign off	

Sokha Jason

Sokha Jason
19 Oct 2023 20:27 PST

Media summary

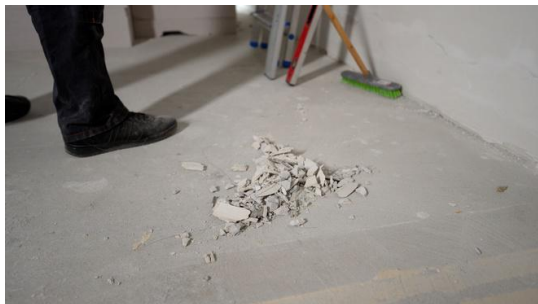


Photo 1
