



General Drone Preflight Checklist

Florence Residences Construction Site

Complete

Score	24 / 26 (92.31%)	Flagged items	0	Actions	1
Drone Model	DJI Mavic 2 Pro				
Flight Type	Land Survey				
Site name	Florence Residences Construction Site				
Date / Time	4 May 2023 07:43 PST				

Actions

1 action

Preflight Check / Site information

Safety signs erected

No

To do | Assignee: SafetyCulture Staff | Priority: Medium | Due: 11 May 2023 10:35 PST | Created by: SafetyCulture Staff

Purchase safety signs at the nearby department store

Preflight Check

1 action, 24 / 26 (92.31%)

Crew

Pilot

Vanessa Larson

Co-Pilot

Mark Campbell

Visual Observer (if applicable)

Weather Information

Cloud Cover % 25

Temperature 72 F

Wind Direction Northeast

Wind Speed 17 mph

Site information 1 action, 7 / 8 (87.5%)

Please check your local drone regulations and check if there are specific regulations that you need to follow.

Checked NOTAMS Yes

Outside required proximity within nearest airport (please check your local regulations on this) Yes

Safe distance from crowds, animals, property Yes

Clear of overhead obstructions (e.g. Buildings, Power lines, Trees, Cell Sites, Houses etc,) Yes

Clear take off and landing site identified Yes




Photo 1

Secondary Landing Zone identified Yes




Photo 2

Home Point identified	Yes
Safety signs erected	No
To do Assignee: SafetyCulture Staff Priority: Medium Due: 11 May 2023 10:35 PST Created by: SafetyCulture Staff	
Purchase safety signs at the nearby department store	
Documents	3 / 3 (100%)
Obtained required airspace authorization (if applicable)	N/A
Obtained operational waiver (if applicable)	Yes
Pilot License (not applicable if drone flight is for government use) on hand	Yes



Photo 3

Drone Flight Equipment Visual Inspection	8 / 9 (88.89%)
Gimbal Lock and Lens Cap REMOVED	Yes
Router and Transmitter ON	Yes
Inspect frame for cracks, loose parts	Safe
Motors able to spin freely	Safe
Propellers and hubs free from cracks or damage	Safe

Check for loose wires and tuck away




Photo 4

Batteries fully charged	Safe
Batteries inserted correctly	Safe
Controller fully charged	Yes
Firmware and Memory	4 / 4 (100%)
Transmitter firmware updated	Yes
Drone firmware updated	Yes
SD card in camera with sufficient memory space	Yes
App updated	Yes
Take-Off	2 / 2 (100%)
Signal and Satellite Strength checked	Yes
Calibrate compass	Yes
Inform spectators (if any)	N/A

Notes

1. Loose wirings were noted but already fixed after issuing action
2. Take extra precaution when flying near the residential building

Pilot's Signature



Vanessa Larson
4 May 2023 10:39 PST

Media summary

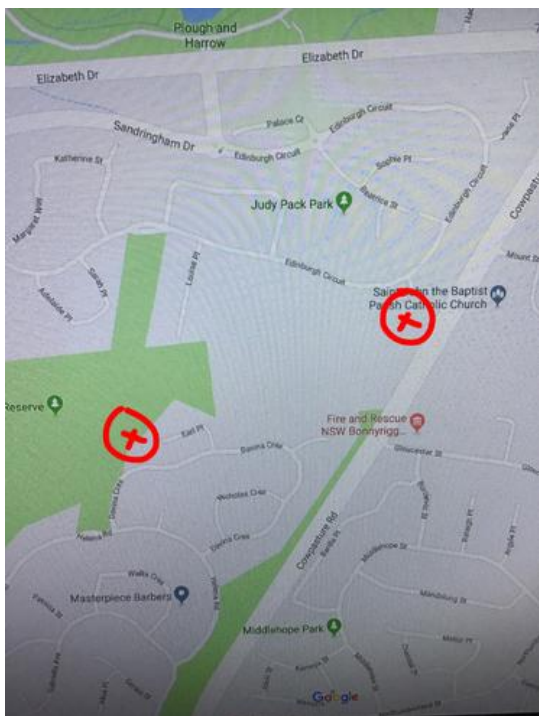


Photo 1

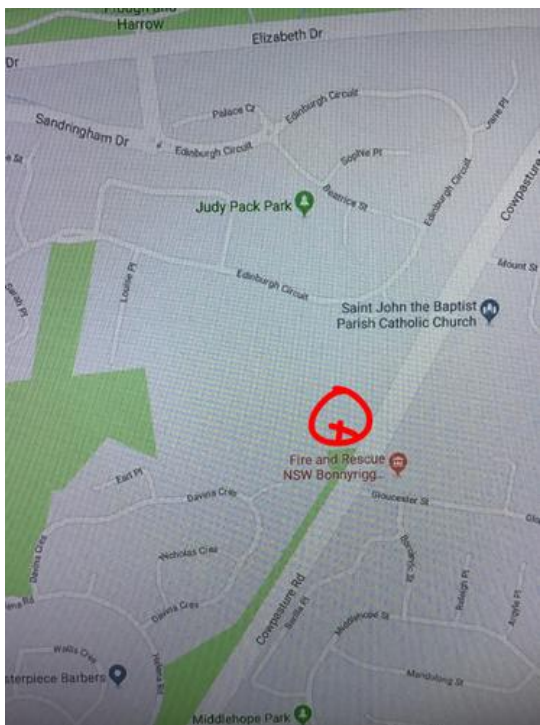


Photo 2

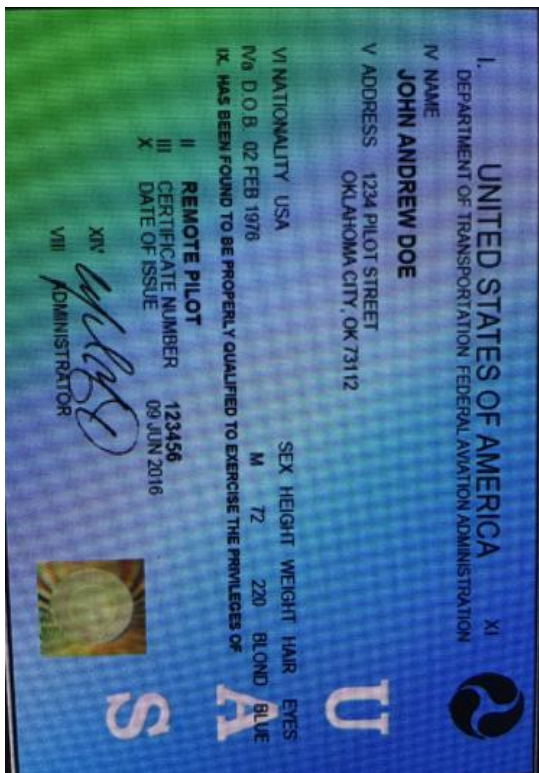


Photo 3

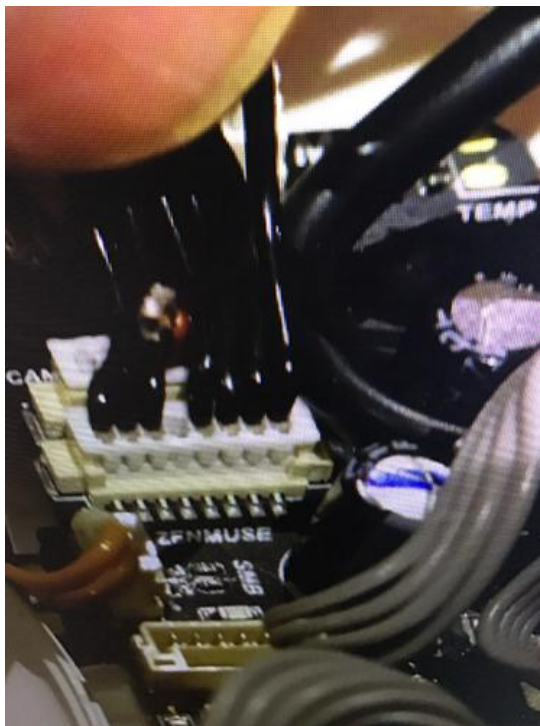


Photo 4
