



ISO Container Inspection Checklist

1 Feb 2023 / EECU322406 / Expert Exporters Co.

Complete

Score	64 / 73 (87.67%)	Flagged items	9	Actions	3
Site conducted	Unanswered				
Shipper	Expert Exporters Co.				
Country of Origin	United States of America				
Container Number	EECU322406				
Inspected by	Sabrina Diaz				
Conducted on	1 Feb 2023 09:30 PST				

Flagged items & Actions

9 flagged, 3 actions

Flagged items

9 flagged, 3 actions

ISO Container Inspection Checklist / Undercarriage

Bottom side rails

Fail



Photo 2

In progress | Assignee: SafetyCulture Staff | Priority: Low | Due: 10 Feb 2023 13:21 PST | Created by: SafetyCulture Staff

Monitor minor damage

ISO Container Inspection Checklist / Doors

Door fittings

Fail

Monitor minor damage



Photo 5

ISO Container Inspection Checklist / Left Side / Interior

Vertical plate

Fail



Photo 6

To do | Assignee: SafetyCulture Staff | Priority: Low | Due: 10 Feb 2023 13:23 PST | Created by: SafetyCulture Staff

Repair left side interior panel

ISO Container Inspection Checklist / Left Side / Exterior

Top side rail

Fail

Monitor minor damage



Photo 7

ISO Container Inspection Checklist / Left Side / Exterior

Panel

Fail

Contain small area of corrosion before it spreads



Photo 8

ISO Container Inspection Checklist / Front Wall / Interior

Light leak

Fail



Photo 9

To do | Assignee: SafetyCulture Staff | Priority: Low | Due: 10 Feb 2023 13:25 PST | Created by: SafetyCulture Staff

Cover roof hole near front wall

ISO Container Inspection Checklist / Floor

Flooring

Fail

Patch this up, make sure no nails are protruding



Photo 11

ISO Container Inspection Checklist / Roof

Roof panel

Fail

This is the root cause for roof hole near the front wall. Repair this as well.



Photo 12

ISO Container Inspection Checklist / Roof

Light leaks

Fail

Other actions

0 actions

ISO Container Inspection Checklist

9 flagged, 3 actions, 64 / 73 (87.67%)

Undercarriage

1 flagged, 1 action, 5 / 6 (83.33%)

Corner fittings

Pass

Bottom end rails

Pass

Still in good condition.



Photo 1

Bottom side rails

Fail



Photo 2

In progress | Assignee: SafetyCulture Staff | Priority: Low | Due: 10 Feb 2023 13:21 PST |
Created by: SafetyCulture Staff

Monitor minor damage

Door sill

Pass



Photo 3

Cross members

Pass

Forklift tunnels

Pass

Doors

1 flagged, 16 / 17 (94.12%)

ISO identification

Pass

Clearly visible ISO marks and CSC plate




Photo 4

CSC safety approval

Pass

Stencils

Pass

Corner posts	Pass
Corner fittings	Pass
Door header	Pass
Door sill	Pass
Door fittings	Fail
Monitor minor damage	
	
Photo 5	
Door lining	Pass
Door gaskets	Pass
Rods	Pass
Rod retainers	Pass
Cams	Pass
Cam retainers	Pass
J-bars	Pass
Rain guttering	Pass
Placard holder	Pass
Left Side	3 flagged, 1 action, 10 / 13 (76.92%)
Interior	1 flagged, 1 action, 4 / 5 (80%)
Plywood lining	Pass
Kick rail	Pass
Vertical plate	Fail
	
Photo 6	
To do Assignee: SafetyCulture Staff Priority: Low Due: 10 Feb 2023 13:23 PST Created	

by: SafetyCulture Staff

Repair left side interior panel

Horizontal rail

Pass

Light leak

Pass

Exterior

2 flagged, 6 / 8 (75%)

ISO identification

Pass

Corner fittings

Pass

Corner posts

Pass

Top side rail

Fail

Monitor minor damage



Photo 7

Bottom side rail

Pass

Forklift pockets

Pass

Panel

Fail

Contain small area of corrosion before it spreads



Photo 8

Placard holder

Pass

Front Wall

1 flagged, 1 action, 10 / 11 (90.91%)

Interior

1 flagged, 1 action, 3 / 4 (75%)

Plywood lining

Pass

Kick plate

Pass

Load bearing surfaces

Pass

Light leak

Fail




Photo 9

To do | Assignee: SafetyCulture Staff | Priority: Low | Due: 10 Feb 2023 13:25 PST | Created by: SafetyCulture Staff

Cover roof hole near front wall

Exterior	7 / 7 (100%)
ISO identification	Pass
Corner fittings	Pass
Corner posts	Pass
Top end rail	Pass
Bottom end rail	Pass
Panel	Pass
Placard holder	Pass
Right Side	13 / 13 (100%)
Interior	5 / 5 (100%)
Plywood lining	Pass
Kick rail	Pass
Vertical plate	Pass
Horizontal rail	Pass
Light leak	Pass
Exterior	8 / 8 (100%)
ISO identification	Pass
Corner fittings	Pass
Corner posts	Pass
Top side rail	Pass

Bottom side rail	Pass
Forklift pockets	Pass
Panel	Pass
	
Photo 10	
Placard holder	Pass
Floor	1 flagged, 4 / 5 (80%)
Flooring	Fail
Patch this up, make sure no nails are protruding	
	
Photo 11	
Floor fasteners	Pass
Threshold plate	Pass
Tie-down devices	Pass
Light leaks	Pass
Roof	2 flagged, 6 / 8 (75%)
ISO identification	Pass
Corner fittings	Pass
Corner posts	Pass
Top end rail	Pass
Bottom end rail	Pass
Roof panel	Fail
This is the root cause for roof hole near the front wall. Repair this as well.	
	
Photo 12	

Roof bows

Pass

Light leaks

Fail

Sign off

I have visually verified to the best of my ability the condition of the container as noted above and found that the container is structurally sound, weather tight, has no false compartments, contains no un-manifested material and the locking mechanisms are in good order.

Additional Recommendations

We should keep on using iAuditor so we can easily identify damages, maximize utilisation of our shipping containers and prevent container fires. Monitor all minor damages and repair roof hole and left side interior panel.

Name & Signature of Inspector



Sabrina Diaz
3 Feb 2023 13:27 PST

Media summary



Photo 1



Photo 2



Photo 3



Photo 4



Photo 5



Photo 6

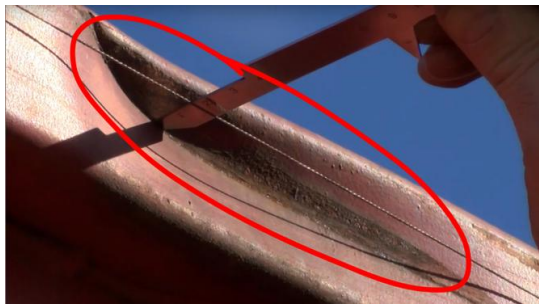


Photo 7



Photo 8



Photo 9



Photo 10



Photo 11



Photo 12
